

**07-121844 ("Rte 5 Widening")
07-LA-5-42.8/47.3
from 5/134 to Magnolia**

ASSISTANT STRUCTURE REPRESENTATIVE REPORT CCO #194

Structure Location & Description of Operation: Providencia OH 53-1085

A) Security Paving removed concrete debris in span 6 left and right sides of the soffit decking under CCO #194.

Track and time for track #2 in span 6, and EIC was Trevors Williams.

Contractor's manlift broke down near the track in Span 7 at 0300.

HOURS-ITEMS NO.											WEATHER	
EQUIPMENT AND/OR LABOR:											Temp 50-70	
EQUIP NO.	NO. MEN	DESCRIPTION (EQUIPMENT/LABOR)	A) CCO #194								Security Paving	REMARKS (Reason for Idleness or other remarks)
	1	carpenter foreman	8.0									Brian Geesaman
	1	carpenter	8.0									Angel Virgen
	1	carpenter	8.0									Anthony Aigamaua
	1	carpenter	8.0									Mike Escamilla
	1	pile butt,	8.0									Manny Centeno
2-1283	1	pickup truck	8.0									F250
34-670	1	forklift	8.0									CAT with bucket
10-676	1	manlift	8.0									60 ft
179	1	flatbed	8.0									F450

I worked from 2100 to 0500, total 8 hours.

Eng Yeong

Eng Yeong


Assist Struct Rep

ASSISTANT STRUCTURE REPRESENTATIVE REPORT

Structure Location & Description of Operation: Providencia OH 53-1085



Removing concrete debris

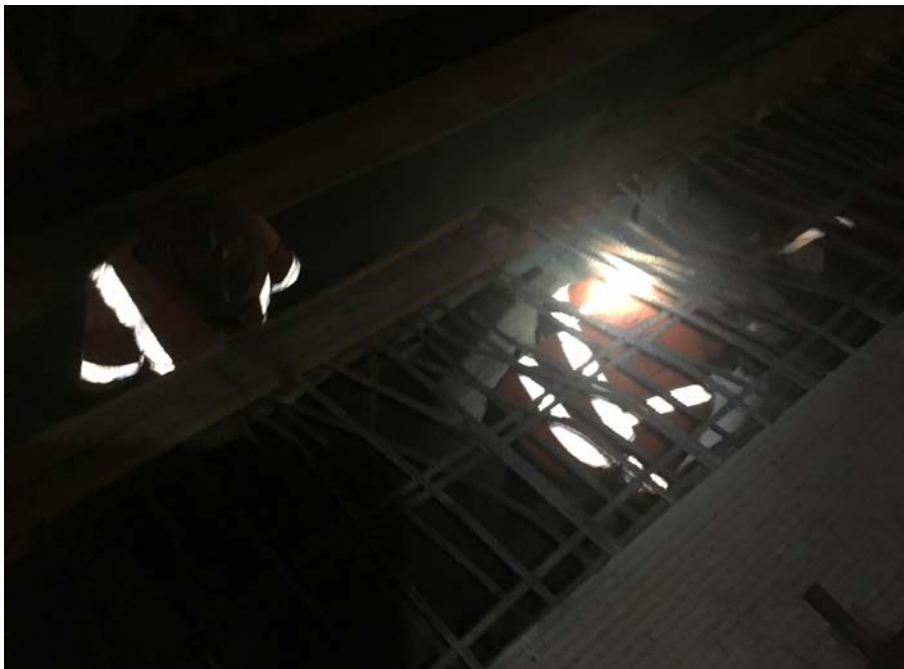

Removing concrete debris

Security Paving Company, Inc.

DAILY FORCE ACCOUNT WORK TENTATIVE AGREEMENT

CONTRACT NO. 07-121844


DATE: ~~7/22/18~~
7/23/18 - 7/24/18

CCO NO. 1941

LOCATION DESCRIPTION OF EXTRA WORK: clean concrete spoil off
of working deck @ providencea Bridge span #6

EQUIPMENT NO	EQUIPMENT	HRS	NO. OF MEN	NAME	HOURS	
					ST	OT
7-1783	F-250	8	1	Ben Grossman	8	
179	F-450	8	1	Anthony Lupone	8	
34-670	CAT FL w/brush	8	1	Robert Esquivel	8	
10-676	Grinder	8	1	Manny Cortez	8	
			1	Angel Vargas	8	

MATERIAL _____



CONTRACTOR'S REPRESENTATIVE

Vanessa
Ly Yang

OWNER'S REPRESENTATIVE
